

 **SIMULATED PROJECT: FICTIONAL COMPANY, CREATED FOR PORTFOLIO AND LEARNING PURPOSES** · Cobbleway Home Services Ltd is not a real business

Project Compass: project status dashboard

Cobbleway Home Services Ltd (fictional) · CRM implementation · Highlight report 5 · Project manager: Chidera Ikenna-Obi (simulated role)

Status date (input)	08 May 2026	Week 10 of 15
---------------------	-------------	---------------

RAG summary

Dimension	RAG	How it is calculated
Schedule	Amber	Worst forecast milestone slip: 0 = G, 1-5 wd = A, >5 wd (tolerance) = R
Cost	Amber	EAC ≤ base = G; within contingency = A; above total budget = R
Scope	Green	Manual: all Must requirements in plan; CR01 approved
Risks	Amber	Open risks scoring 15+: 0 = G, 1 = A, 2+ = R
Issues	Amber	Any open High issue = A

Milestone tracker

Milestone	Baseline	Forecast / actual	Variance (wd)	Status	RAG
M1 Charter and business case approved	11 Mar 2026	11 Mar 2026	0	Achieved	Green
M2 Requirements signed off	24 Mar 2026	24 Mar 2026	0	Achieved	Green
M3 Supplier selected and contract signed	07 Apr 2026	07 Apr 2026	0	Achieved	Green
M4 Configuration complete	12 May 2026	12 May 2026	0	On track	Green
M5 Go/no-go decision	18 May 2026	22 May 2026	4	Forecast late	Amber
M6 Go-live	20 May 2026	27 May 2026	4	Forecast late	Amber
M7 Project closed	10 Jun 2026	16 Jun 2026	4	Forecast late	Amber

Budget vs actual (GBP)

Category	Budget	Actual to date	Forecast (EAC)	Variance	% spent
CRM licences (18 users, year 1)	£6,800	£6,800	£6,800	£0	100.0%
Supplier configuration and integration	£9,500	£7,600	£10,400	£900	80.0%
Data migration and cleansing	£4,200	£4,200	£4,900	£700	100.0%
Training and materials	£3,000	£600	£3,000	£0	20.0%
Internal staff time (backfill)	£6,000	£3,900	£6,300	£300	65.0%
Hardware (6 rugged tablets and cases)	£3,500	£3,380	£3,380	-£120	96.6%
Base budget total	£33,000	£26,480	£34,780	£1,780	80.2%

PM commentary (status date)

Amber overall. Data cleansing (task 4.1) is forecast to finish 10 working days late because ~18% of legacy records are duplicates (issue IO1). Go-live is forecast for 27 May against a 20 May baseline: a 4 working-day slip, inside the 1-week tolerance. CR01 (accounting connector, £900) approved. EAC is £1,780 over base budget and within contingency. Decision needed: none. Next: complete cleansing, trial migration, UAT from 19 May.

Issues at status date

Issue	ID	Severity	Raised	At status date
Around 18% of legacy customer records are duplicates	IO1	High	21 Apr 2026	Open
Accounting package needs a paid connector for invoice sync	IO2	Medium	16 Apr 2026	Closed
Two tablets faulty on delivery	IO3	Low	06 May 2026	Open
UAT: VAT rounding error on quote PDF template	IO4	Medium	20 May 2026	Not yet raised

Next fortnight

- Finish data cleansing (4.1) and run trial migration with reconciliation (4.2)
- Complete configuration (M4, 12 May); tablets enrolled and tested offline
- Office and field training 14–15 May; UAT 19–22 May; go/no-go 22 May

Overall RAG	Amber
-------------	-------



Key figures

Total budget (incl. contingency)	Actual spend to date	Forecast at completion
£36,500	£26,480	£34,780
Contingency remaining	Milestones achieved	Open risks
£1,720	43%	8

Risk heatmap (open risks at status date)

Probability ↓ Impact →	1	2	3	4	5
5					
4				1	
3		1	2	1	
2				2	1
1					

Numbers = count of open risks in each cell. Source: Risks sheet (from the RAID log).

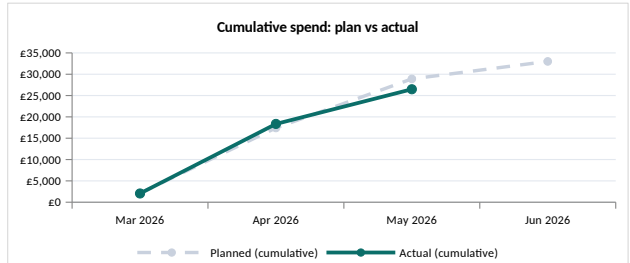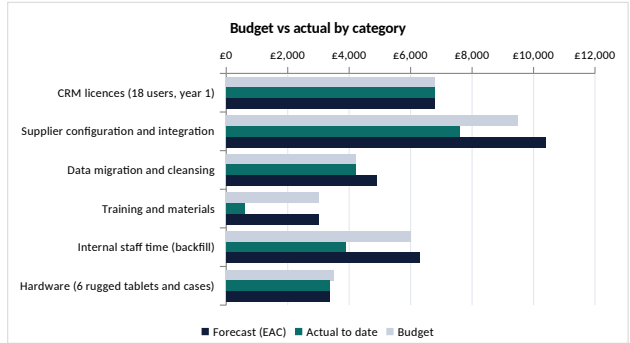

 **SIMULATED PROJECT: FICTIONAL COMPANY, CREATED FOR PORTFOLIO AND LEARNING PURPOSES • Cobbleway Home Services Ltd is not a real business**

Milestone data

Forecast = latest forecast at the status date (actual if achieved).

WBS	Milestone	Baseline	Forecast / actual	Variance (wd)
1.4	M1 Charter and business case approved	11 Mar 2026	11 Mar 2026	0
2.3	M2 Requirements signed off	24 Mar 2026	24 Mar 2026	0
2.5	M3 Supplier selected and contract signed	07 Apr 2026	07 Apr 2026	0
3.6	M4 Configuration complete	12 May 2026	12 May 2026	0
5.3	M5 Go/no-go decision	18 May 2026	22 May 2026	4
7.2	M6 Go-live	20 May 2026	27 May 2026	4
8.3	M7 Project closed	10 Jun 2026	16 Jun 2026	4

 **SIMULATED PROJECT: FICTIONAL COMPANY, CREATED FOR PORTFOLIO AND LEARNING PURPOSES • Cobbleway Home Services Ltd is not a real business**

Budget vs actual (GBP)

Actual to date at status date 08 May 2026. EAC = estimate at completion.

Category	Budget	Actual to date	Forecast (EAC)	Variance (EAC – budget)	% spent
CRM licences (18 users, year 1)	£6,800	£6,800	£6,800	£0	100.0%
Supplier configuration and integration	£9,500	£7,600	£10,400	£900	80.0%
Data migration and cleansing	£4,200	£4,200	£4,900	£700	100.0%
Training and materials	£3,000	£600	£3,000	£0	20.0%
Internal staff time (backfill)	£6,000	£3,900	£6,300	£300	65.0%
Hardware (6 rugged tablets and cases)	£3,500	£3,380	£3,380	-£120	96.6%
Base budget total	£33,000	£26,480	£34,780	£1,780	80.2%
Contingency (10.6% of base)	£3,500				
Total approved budget (incl. contingency)	£36,500				
Contingency remaining at EAC	£1,720				

⚠ SIMULATED PROJECT: FICTIONAL COMPANY, CREATED FOR PORTFOLIO AND LEARNING PURPOSES • Cobbleway Home Services Ltd is not a real business

Cumulative spend profile (GBP)

Actual for May is to the status date only.

Month	Planned (cumulative)	Actual (cumulative)
Mar 2026	£2,100	£2,050
Apr 2026	£17,400	£18,350
May 2026	£28,900	£26,480
Jun 2026	£33,000	

 **SIMULATED PROJECT: FICTIONAL COMPANY, CREATED FOR PORTFOLIO AND LEARNING PURPOSES • Cobbleway Home Services Ltd is not a real business**

Risk data (copy of RAID log risks)

Heatmap counts risks open at the status date: raised on or before it and not closed by then.

ID	Risk	Raised	Prob.	Impact	Score	Closed
R01	Poor legacy data quality delays migration	09 Mar 2026	4	4	16	18 May 2026
R02	Field engineers do not adopt the mobile app	09 Mar 2026	3	4	12	
R03	Accounting integration more complex than quoted	23 Mar 2026	3	4	12	27 Apr 2026
R04	Key staff unavailable for UAT and training	16 Mar 2026	3	3	9	15 May 2026
R05	Supplier resourcing slips configuration	02 Apr 2026	2	4	8	12 May 2026
R06	Customer data migrated without proper retention review	16 Mar 2026	2	5	10	27 May 2026
R07	Change requests push cost over tolerance	13 Apr 2026	3	3	9	16 Jun 2026
R08	Low mobile signal stops job updates	23 Mar 2026	3	2	6	15 May 2026
R09	Go-live disrupts customer service	20 Apr 2026	2	4	8	10 Jun 2026

 **SIMULATED PROJECT: FICTIONAL COMPANY, CREATED FOR PORTFOLIO AND LEARNING PURPOSES • Cobbleway Home Services Ltd is not a real business**

Issue data (copy of RAID log issues)

ID	Issue	Raised	Severity	Closed
I01	Around 18% of legacy customer records are duplicates	21 Apr 2026	High	13 May 2026
I02	Accounting package needs a paid connector for invoice sync	16 Apr 2026	Medium	27 Apr 2026
I03	Two tablets faulty on delivery	06 May 2026	Low	12 May 2026
I04	UAT: VAT rounding error on quote PDF template	20 May 2026	Medium	22 May 2026

⚠ SIMULATED PROJECT: FICTIONAL COMPANY,
CREATED FOR PORTFOLIO AND LEARNING PURPOSES •
Cobbleway Home Services Ltd is not a real business

UK bank holidays

Date	Holiday
03 Apr 2026	Good Friday
06 Apr 2026	Easter Monday
04 May 2026	Early May bank holiday
25 May 2026	Spring bank holiday
